Project Management Plan (PMP)

Project Name: Maternity Stream System (MSS)
Organization: Maternity Stream International Pty Ltd (MSI)

Table of Contents

1 Project Overview – What Are We Doing 2
2 Project Deliverables 2
3 Project Scope 4
3.1 Project Scope 4
3.2 Exclusions 5
3.3 Interface with Other Sub-Projects 5
3.4 Key Dependencies 5
3.5 Project Constraints 6
3.6 Issues Management 6
4 Scheduling 6
4.1 Project Schedule 7
4.2 Project Milestones 8
5 Project Governance 10
5.1 Project Team 10

5.2 Project Team Structure 14
6 Stakeholders 15
7 Communication Approaches 16
7.1 Internal communication 16
7.2 External communication 17
8 Change Management Plan 18
8.1 Change Control Process 18
8.2 Change Request Authority 19
8.3 Change Tracking and Communication 19
9 Quality Management Plan 20
9.1 Quality Expectations and Standards 20
9.2 Quality Assurance and Quality Control 22
10 Sustainability Management Plan 23
11 Project Budget 26

1 Project Overview – What Are We Doing

This Project Management Plan (PMP) relates to MSS Sub-Project II: Network Infrastructure Upgrade and Sub-Project III: Data Migration, which are being considered for implementation by MSI. The purpose of this document is to provide a clear overview of the key issues that need to be considered, enabling stakeholders to understand how these projects should be planned, managed, and implemented.

These two sub-projects are essential to the successful and efficient implementation of the MSS platform. The existing network infrastructure was not designed to support the performance, scalability and security requirements of the proposed platform. Furthermore, existing health data stored across current systems must be accurately and securely migrated before the platform can go live. Sub-Project II, delivered by contractor DCPlus, will upgrade and extend the network environment through current-state auditing, requirements analysis, logical and physical design, procurement, installation and testing. Sub-Project III, delivered by contractor DemSet, will manage the end-to-end migration of health data through data mapping, quality assessment, cleansing, testing, and reconciliation.

The key objective of PMP is to outline strategic approaches for designing, developing and delivering the two sub-projects, with the objective of establishing a secure and reliable network foundation and completing a fully validated data migration within the agreed timeframe and budget. Ultimately, these activities will support the successful and well-prepared go-live of the MSS platform.

2 Project Deliverables

WS1: Management, Monitoring & Controls

- Business Case document
- RFT documentation and evaluation records
- Approved project charter and sub-project management plan
- Steering Committee meeting minutes and reporting pack
- Project status/performance reports (financial and resource management)
- Change control log and change requests
- Operational readiness support materials (contribution to OSG, as-built documentation, handover support)
- Project Close Out Report
- Benefits Tracking/Realisation report

WS2: Business Change Management (BCM)

- Stakeholder map/analysis
- Change management strategy
- Change impact analysis
- Training need analysis
- Training Plan
- Communications Plan
- Stakeholder Engagement Plan
- Business Alignment Plan
- Readiness Assessment (initial and updated)
- Training collateral (materials, guides)
- Communications collateral (announcements, FAQs, updates)
- Business alignment collateral
- Transition Plan

WS3 (Sub-Project II): Network Infrastructure

- Current State Assessment and existing infrastructure inventory (existing hardware, topology, performance audit)
- Business and Technical Requirements Analysis report
- Gap Analysis report
- High-Level Network Architecture Design
- Network Architecture & Infrastructure Logical Design (IP addressing/VLAN plan, load-balancing strategy, security zones)
- Network Architecture & Infrastructure Physical Design (physical requirements, site survey, topology and rack diagrams, cable management plan)
- Procurement documentation and Bill of Materials (hardware/software specifications)
- Installed and configured network hardware (routing, switching, wireless, firewall, redundancy, load-balancing)
- Network Testing and Validation reports (performance, failover/redundancy, security penetration testing)
- Configuration and network diagram documentation

- Rollback and contingency plan, cutover/migration schedule
- Post-implementation monitoring report
- IT staff and end-user training records
- Post-project review and lessons learnt report

WS4 (Sub-Project III): Data Migration

- Data migration scope and initial analysis
- Existing data assessment and high-level data mapping
- Initial assumptions, constraints and data quality risk log
- Detailed data mapping specifications
- Data quality assessment report
- Data migration strategy and approach document
- Migration environment definition and schedule
- Data cleansing rules and cleansed/validated data set
- Migration tools/scripts
- Test environment migration and SME verification results
- Cutover plan for production migration (blackout windows, downtime, rollback plan)
- Production data load and performance monitoring report
- Reconciliation report (record counts, accuracy and integrity validation)
- Business Process Validation
- Final Stakeholder/CIO Sign-off
- Data Migration Final Report
- Lessons Learned Documentation

WS5: Security

- IT Security Control Assessment report
- Identity and Access Management (IAM) design — physical and network
- IAM build/implementation — physical and network
- Physical Access Controls installation records
- Security policy and protocol documentation
- Security Completion Report

WS6: Operational Readiness

- Service Design document
- Operational Support Guide (OSG)
- As-Built Documentation
- Handover to Support (P2S) package
- Go-live Checklist (completed and signed off)
- Go-live Approval record
- Warranty/Hypercare support plan and log

3 Project Scope

3.1 Project Scope

The scope of this phase of MSS implementation covers the design, build and validation of a scalable network environment alongside the planning, cleansing and transferring of the existing patient data into the new system. Alongside sub-projects II and III, the supporting workstreams cover project management and control (WS1), business change management (WS2), security (WS5) and operational readiness (WS6).

Sub-project	Workstream	Description
Sub-Project II	WS3: Network Infrastructure	The key objective is to deliver and install a network infrastructure that can support the MSS platform. The workstream also aims to provide a strategically tested and validated and a fully documented, monitored network environment ready for ongoing operation.
Sub-Project III	WS4: Data Migration	The key objective is to deliver a complete, accurate and validated transfer of existing patient data into the MSS platform, ensuring the migrated data is reliable, processed and ready to support live clinical and business operations from go-live.

3.2 Exclusions

- Development, coding and modification of the MSS application are excluded, as these activities belong to Sub-Project I.
- Major changes to existing maternity service processes, organisational procedures or business workflows are excluded.
- Designing or developing new features, modules, or business functionality for the MSS platform is outside the scope of these sub-projects.
- The Data Migration workstream will migrate and validate existing health data but will not create new health records or generate new clinical data.
- Purchasing hardware, software or equipment not directly required for the network infrastructure upgrade is excluded.

3.3 Interface with Other Sub-Projects

Sub-Project II and Sub-Project III provide the technical foundation required for the proper development of Sub-Project I. The agile team (DocCloud and StreamTech) relies on these sub-projects for end-to-end integration and testing: representative data from WS4 test-environment migration is available from 30 April 2027, and WS3 network is installed and commissioned by 31 August 2027, ahead of final integrated testing before Go-Live on 30 September 2027. Specifically, the SaaS MSS tenant configuration and integration testing (EHR, lab systems, billing platforms) rely on network connectivity established by DCPlus and on representative datasets prepared through the DemSet migration process. On top of that, Sub-Project I's evolving functional and integration requirements including API endpoints, security requirements inform the design decisions made in WS3 and WS4. The three sub-projects therefore run in parallel but are tightly intertwined at key milestones, particularly the execute stage gate for Sub-Projects II and III and Go-live Approval, where all three workstreams must converge on a tested and integrated environment.

3.4 Key Dependencies

- DocCloud's SaaS platform decisions and API specifications must be finalised before StreamTech can configure integrations.
- MSI's procurement of core hardware and servers must be completed early, as DCPlus and DemSet require this equipment in their development and test environments before installation and testing can begin. Development/test environment equipment must be in place by January 2027 for the WS4 test-environment migration, ahead of the main WS3 procurement of materials (March - June 2027)
- StreamTech's SaaS configuration, workflow customisation, and integration testing cannot be fully validated until the network infrastructure is installed and the test-environment data migration is complete.
- Identity and Access Management (WS5) build activities rely on WS3's network architecture being finalised, since access controls are layered onto the network design.
- DCPlus's ability to deliver network bandwidth depends on existing telco service agreements.
- DemSet's security protocol delivery is scheduled for distribution to StreamTech and other stakeholders, creating a timing dependency for broader system security alignment .

3.5 Project Constraints

- The third-party vendors including DocCloud, StreamTech, DemSet, DCPlus must coordinate schedules and interfaces, introducing communication and integration overhead outside MSI's direct control. Delivery heavily depends on coordination across these four contractors. This introduces scheduling and communication dependencies outside MSI's direct control.
- As a healthcare data migration project, the work is subject to compliance obligations such as the Privacy Act, which constrains how patient data can be handled, tested and stored throughout WS4.
- Stage-gate approvals are fixed points in the timeline, limiting flexibility to absorb delays without impacting downstream workstreams.
- Per the project timeline, execution activities in WS3 and WS4 cannot commence until the production environment exists. If this environment is delayed, technical execution across both sub-projects is blocked.
- MSI is responsible for procuring servers, routers, firewalls and other equipment, and this must occur earlier than standard deployment timing so that teams can use this equipment in their development/test environments. Delays in MSI's procurement process would constrain all downstream technical work.
- MSI has stated an intent to minimise customisation to the SaaS platform wherever possible to reduce the risk of implementation failure. This constrains how much the platform can be tailored to MSI-specific workflows and any customisation must remain within limits allowed by DocCloud as the vendor.

3.6 Issues Management

The project will maintain a centralised issue register, accessible to the Project Manager and all the team members. The register will be reviewed in the fortnightly project team meeting. The process follows four stages:

- Any team member can raise an issue at any time. Issues are logged in the centralised issue register document with a description, date raised, source and initial severity rating

- At the fortnightly project team meeting, the Project Manager, supported by relevant team members will review newly logged issues, assesses their impact on schedule, cost and quality, and assigns a priority level in the register
- Progress on open issues will be reviewed at each fortnightly project team meeting, with status updates logged directly in the document, unresolved issues will be carried forward until closed
- Issues that cannot be resolved or that pose a critical risk to project milestones, will be transferred from the project meeting to the Steering Committee for decision-making authority. Issues involving security or compliance will be transferred directly to Don Lemon (Security Implementation Consultant) for review. All escalations and their outcomes will be recorded in the Issues Register to maintain a complete audit trail

4 Scheduling

4.1 Project Schedule

This schedule covers the two sub-projects in scope: Sub-Project II, WS3 Network & Infrastructure, delivered by DCPlus, and Sub-Project III, WS4 Data Migration, delivered by DemSet. Both follow a plan-driven (stage-gate) approach from August 2026 to November 2027. Each Sub-Project moves through Initiation, Scoping, Planning & Design, Execution and Close Out, and three approval points control the schedule. Stage Gate approval (Business Case) on 30 October 2026 closes Scoping and begins Planning and Design. Stage Gate approval (Execute) on 30 April 2027 closes Planning & Design and Begins Execution. The Go-Live approval on 30 September 2027 marks the end of Execution and begins Close-Out. Figure 1 summarises the timeline, work elements and key milestones.

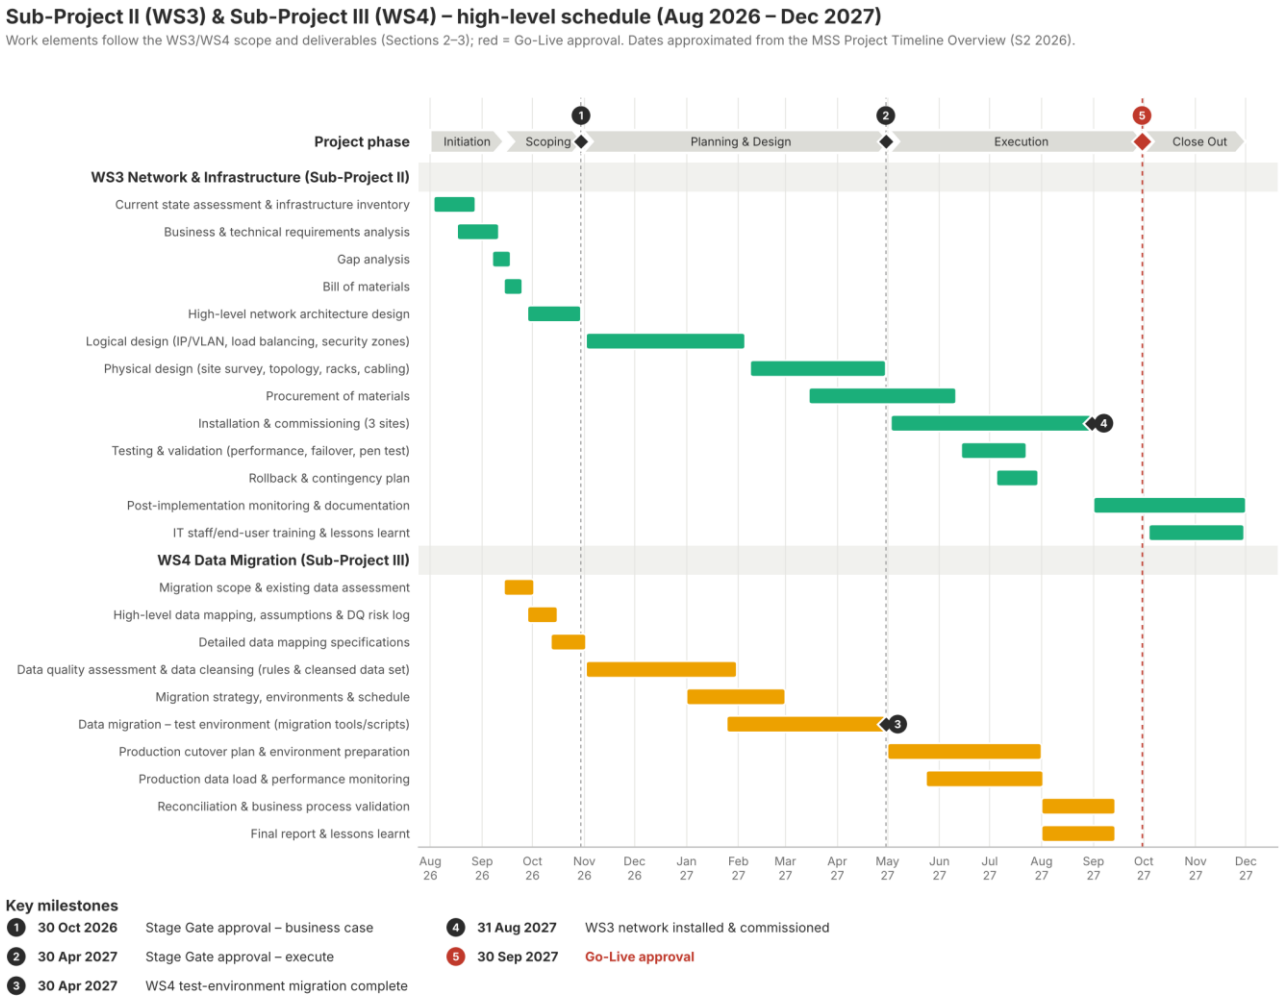


Figure 1: High-level project schedule for Sub-Project II (WS3 Network & Infrastructure) and Sub-Project III (WS4 Data Migration), August 2026 – December 2027

WS3 Network & Infrastructure. Work starts with the current-state assessment and infrastructure inventory in August 2026. The business and technical requirements analysis, gap analysis and bill of materials follow, all completed by the end of September 2026, before any design work begins. The high-level network architecture design runs from late September to the business-case stage gate on 30 October 2026 (milestone 1). The logical design (IP addressing/VLAN plan, load balancing and security zones) follows from November 2026 to February 2027. The physical design (site survey, topology and rack diagrams, cable management) runs from February to April 2027. Procurement of materials begins in March 2027, so core hardware is available straight after the execute stage gate on 30 April 2027 (milestone 2), which meets the early-procurement dependency in Section 3.4. Installation and commissioning across the three sites runs from May to the end of August 2027. Testing and validation (performance, failover and penetration testing) and the rollback and contingency plan are completed during installation, before August 2027. The network is fully installed and commissioned by 31 August 2027 (milestone 4), a month ahead of Go-Live approval (milestone 5). Post-implementation monitoring and final documentation (configurations, network diagrams and IP plans) run from September to the start of December 2027. IT staff and end-user training and the lessons-learnt review run alongside them, and the post-project review is completed by 30 November 2027.

WS4 Data Migration. Work starts in mid-September 2026 with the migration scope and existing data assessment. The high-level data mapping (initial assumptions, constraints and the data-quality risk log) and the detailed data mapping specifications follow, all completed by the start of November 2026. The data quality assessment and data cleansing run from the start of November 2026 to the end of January

2027 and produce the cleansing rules and a cleansed, validated data set. The migration strategy, environments and schedule are defined from January to the start of March 2027, so the team can prepare for migration early. The test-environment migration runs from late January to the end of April 2027: the migration tools and scripts are built, run against the test environment and verified by SMEs. It finishes on 30 April 2027 (milestone 3), in time for the execute stage gate (milestone 2). From May to the start of August 2027, the production cutover plan (blackout windows, downtime and rollback) is prepared and the production environment readied, while the production data load is carried out and its performance monitored. Reconciliation and business process validation then run from 1 August to 14 September 2027. This confirms record counts, data accuracy and integrity, and that the migrated data supports MSI's business processes, leading to CIO sign-off. The final report and lessons learnt are completed by the same date, two weeks before Go-Live approval on 30 September 2027 (milestone 5).

The schedule is built around five key milestones:

1. 30 October 2026: Stage Gate approval for the business case, which closes Scoping and authorises detailed planning and design.

2. 30 April 2027: Stage Gate approval to execute, which closes Planning & Design and allows procurement, installation and the production migration to proceed.

3. 30 April 2027: WS4 test-environment migration complete, which confirms the migration tools and scripts are ready for production.

4. 31 August 2027: WS3 network installed and commissioned across all three sites.

5. 30 September 2027: Go-Live approval.

Go-Live approval is the critical milestone, as all Sub-Projects (I, II and III) must all converge on it. WS3 commissioning and WS4 reconciliation and CIO sign-off (14 September 2027) are therefore scheduled ahead of it, to leave a buffer for any late issues. The planned end date for Sub-Projects II and III is 30 November 2027, when WS3 post-implementation monitoring, documentation and the post-project review are complete and both sub-projects are formally closed.

4.2 Project Milestones

The table below sets out the milestones that mark the completion of each stage of Sub-Project II (WS3) and Sub-Project III (WS4). Milestones are listed separately for each workstream and include the key milestones shown in Figure 1 and the milestone that marks the completion of each workstream. For each milestone it gives the criteria that must be met, the responsible owner and the estimated due date, in line with the project timeline.

Workstream	Milestone	Success Criteria	Owner	Estimated due date
WS3 Network & Infrastructure	Stage Gate approval – business case (key milestone 1)	Current-state assessment Business/technical requirements and gap analysis Bill of materials High-level network design complete and reviewed	Catherine Dobbs (DCPlus) Approved by Ben Dover (Sponsor/CIO)	30 Oct 2026

		Steering Committee approval recorded		
WS3 Network & Infrastructure	Stage Gate approval – execute (key milestone 2)	Logical and physical designs approved Procurement of materials under way Production environment available for execution Steering Committee approval recorded	Catherine Dobbs (DCPlus) Approved by Ben Dover (Sponsor/CIO)	30 Apr 2027
WS3 Network & Infrastructure	Network installed & commissioned (key milestone 4)	Hardware installed and configured at all three sites Performance, failover and penetration tests passed with no open critical/high defects Rollback and contingency plan approved	Catherine Dobbs (DCPlus) QA sign-off by Ash Mclelland	31 Aug 2027
WS3 Network & Infrastructure	Go-Live approval (key milestone 5)	Network stable in production and ready to support MSS No open critical network or security defects WS3 readiness confirmed on the go-live checklist Go-Live approved	Catherine Dobbs (DCPlus) with Afra Binte Azad (PM) Approved by Ben Dover	30 Sep 2027
WS3 Network & Infrastructure	Post-implementation monitoring and post-project review complete (WS3 completion)	Network stable after Go-Live (≥ 99.5% availability, no Severity 1 incidents) Configurations, network diagrams and IP plans finalised and handed over IT staff and end users trained Lessons-learnt report accepted	Catherine Dobbs (DCPlus) with Afra Binte Azad (PM)	30 Nov 2027
WS4 Data Migration	Stage Gate approval – business case (key milestone 1)	Migration scope and existing data assessment complete High-level data mapping, initial assumptions/ constraints and data-quality risk log documented Steering Committee approval recorded	Perera Kinley (Data Migration Expert) with Pardeep Kaur (DemSet) Approved by Ben Dover	30 Oct 2026
WS4 Data Migration	Test-environment migration complete (key milestone 3)	Migration tools/scripts run successfully in the test environment SME and user verification passed Defects resolved Scripts approved for production use	Perera Kinley with Pardeep Kaur (DemSet)	30 Apr 2027

WS4 Data Migration	Stage Gate approval – execute (key milestone 2)	Detailed mapping specifications, data quality assessment and cleansing complete Migration strategy, environments and schedule approved Test migration passed Steering Committee approval recorded	Perera Kinley Approved by Ben Dover (Sponsor/CIO)	30 Apr 2027
WS4 Data Migration	Production data reconciled and signed off (WS4 completion)	Record counts reconcile 100% Data error rate below 1% Business process validation passed CIO sign-off obtained Final report and lessons learnt accepted	Perera Kinley Sign-off by Ben Dover (CIO)	14 Sep 2027
WS4 Data Migration	Go-Live approval (key milestone 5)	Migrated data live and verified in the production MSS environment No open critical data defects WS4 readiness confirmed on the go-live checklist Go-Live approved	Perera Kinley with Pardeep Kaur (DemSet) Approved by Ben Dover	30 Sep 2027

5 Project Governance

5.1 Project Team

Key Project Team Members (Internal)		
Name	**Role(s)**	**Skill/Responsibilities**
Afra Binte Azad	Project Manager	• Act as the primary point of contact between the Steering Committee, contractors and internal stakeholders • Report project progress and performance to the Project Sponsor on a regular basis • Plan, coordinate and oversee delivery of Sub-Project II and Sub-Project III from initiation to closure • Identify, monitor and mitigate project risks and issues, escalating where necessary
Mr. Ben Dover	Project Sponsor & CIO	• Approve key project decisions, stage gates and changes to scope, budget or timeline • Receive and review progress updates from the Project Manager and Product Manager at fortnightly or monthly progress reviews • Manage escalations that exceed the Project Manager's authority


		• Own overall accountability for the project's alignment with MSI's digital transformation strategy
Mrs. Donna Jenner	Founder & CEO	• Review and approve high-level project outcomes at quarterly reviews and major milestones • Represent the project to the Board and external stakeholders as needed • Act as final decision-maker on matters escalated beyond the Project Sponsor • Support strategic pivots in project direction where required
Dr. Sara Adams	Product Manager	• Define and maintain the overall MSS product strategy and roadmap across all sub-projects • Provide input into prioritisation decisions affecting Sub-Projects II and III • Ensure that network infrastructure and data migration deliverables align with the broader MSS product vision • Review and endorse key deliverables before they are escalated to the CIO/Steering Committee
Ash Mclelland	QA and Test Lead	• Develop and coordinate the test strategy and test plans for network infrastructure and data migration deliverables • Design test cases and conduct performance, failover, security and data quality testing • Report testing outcomes, defects and risk assessments to the Project Manager • Set up and manage test environments for infrastructure validation and data migration testing • Ensure quality criteria are reflected in test planning and acceptance criteria • Monitor adherence to project governance, templates and documentation standards • Establish and maintain quality standards and processes across all project deliverable
Don Morrison	Security and Compliance Expert	• Define security requirements and controls for the network infrastructure and migrated data • Ensure compliance with relevant healthcare and privacy standards including Australian Privacy Principles, HL7, FHIR etc • Conduct security risk assessments and support security penetration testing activities

		• Develop and maintain the incident response plan for the MSS environment
Bill Sykes	Legal Support	• Draft, review, and negotiate contracts with third-party providers • Advise the Project Manager on contractual risks, obligations and compliance requirements • Assist in resolving contractual disputes or variations that arise during project execution • Develop licensing agreements required for client and vendor engagement
Perera Kinley	Data Migration Expert	• Lead the design and execution of the data migration strategy and approach for WS4 • Coordinate reconciliation and validation activities to confirm data accuracy and completeness • Oversee data mapping, data quality assessment, and cleansing activities • Provide subject matter expertise and guidance to DemSet and internal stakeholders throughout the migration lifecycle
Don Lemon	Security Implementation Consultant	• Monitor the implementation of the MSS security system across the network infrastructure and migrated data • Ensure the security solution meets the required standards, including the Privacy Act and Australian Privacy Principles • Review security and compliance issues escalated through the issue register (Section 3.6) • Work with Don Morrison and DemSet to confirm security controls are in place before Go-Live
Key Project Team Members (External)		
Name	**Role(s)**	**Skill/Responsibilities**
Roy Clark	Project Lead (StreamTech)	• Configure workflows for appointment scheduling, billing, virtual consultations and information exchange to match MSI's requirements • Develop and test integrations between the SaaS platform and other systems including EHR, lab systems, billing platforms • Carry out any necessary platform customisation within agreed project scope, while minimising customisation to preserve SaaS benefits and reduce delivery risk

		• Configure and populate the testing environment with representative data for validation
Pardeep Kaur	Team Lead (DemSet)	• Plan and execute the migration of existing patient data to the MSS platform, including data cleansing, transformation and validation • Design and deliver Disaster Recovery (DR) systems for patient data, using standard replication protocols • Develop a standard set of security protocols and systems to be implemented and monitored across the entire platform • Share the finalised security plan with StreamTech and other relevant stakeholders on an agreed schedule • Support reconciliation and sign-off activities to confirm migrated data is accurate, complete and fit for go-live
Catherine Dobbs	Client Manager (DCPlus)	• Assess the existing network infrastructure's capacity, security, and compatibility with the SaaS application • Design a scalable network infrastructure capable of accommodating future growth and increased user traffic • Document network configuration, security measures, and troubleshooting procedures • Coordinate provision of network bandwidth and connectivity, leveraging existing fibre capacity, redundancy and telco service agreements to support future MSS expansion

5.2 Project Team Structure

The figure below illustrates the organisational structure that is proposed for coordinating the Project. This organisational structure is described below the diagram.

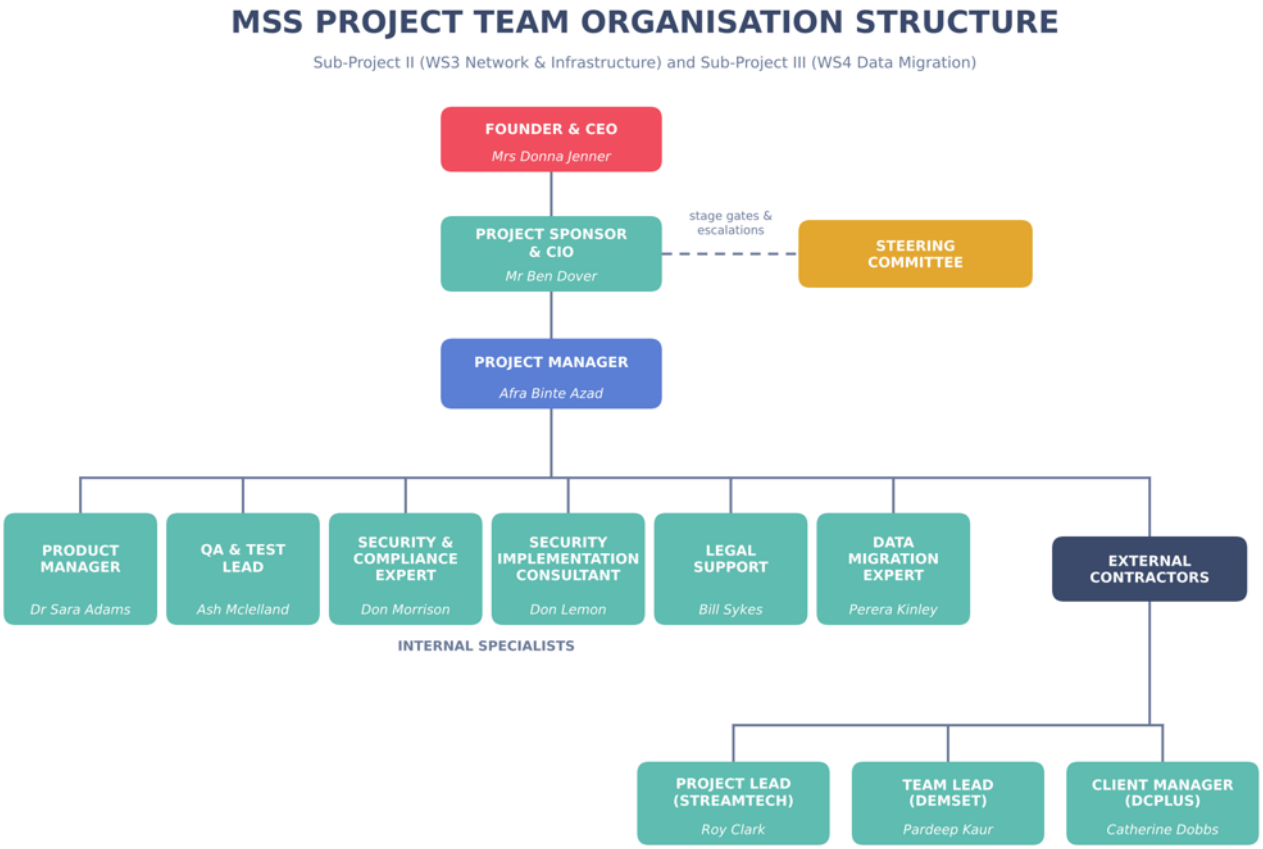

The proposed project team structure establishes clear lines of responsibility, communication and escalation between the team members. At the highest level, the Founder and CEO, Mrs. Donna Jenner, provides executive oversight and acts as the final escalation point for major strategic decisions. The Project Sponsor and CIO, Mr. Ben Dover, is responsible for project governance, approving significant decisions and managing escalations that exceed the Project Manager's authority. The Sponsor works with the Steering Committee, which includes the CEO and CIO as standing members, to approve stage gates and decide on issues and changes escalated from the project.

The project manager is responsible for coordinating the day-to-day delivery of the project and acts as the main point of contact between the Project Sponsor, internal specialists and external contractors. All major project workstreams are coordinated through the Project Manager, who monitors progress, risks, issues, quality and delivery against the approved scope, schedule and objectives.

The internal specialists provide expertise and assurance across the project. Dr. Sara Adams, Product Manager, maintains alignment with the overall product strategy and provides input into prioritisation and major deliverables. Ash Mclelland (QA and Test Lead), Don Morrison (Security & Compliance Expert), Don Lemon (Security Implementation Consultant), Bill Sykes (Legal Support) and Perera Kinley (Data Migration Expert) provide specialist support for quality assurance and testing, security and privacy compliance, monitoring of the security implementation, contracts and licensing, and data migration respectively. These specialists communicate with the Project Manager and relevant external contractors to ensure that technical deliverables meet MSI's requirements.

The external contractors are responsible for delivering specialised components of the project under the coordination of the Project Manager. Catherine Dobbs from DCPlus leads Sub-Project II

(WS3), covering network assessment, design, installation, commissioning and connectivity. Pardeep Kaur from DemSet leads Sub-Project III (WS4), covering the migration of existing patient data (cleansing, transformation, validation and reconciliation) as well as disaster recovery and security protocols. Roy Clark from StreamTech leads SaaS configuration and system integration for Sub-Project I, which interfaces with both sub-projects. Although these external stakeholders are not directly controlled by MSI, their project responsibilities, deliverables and communication requirements are coordinated through the Project Manager.

This structure provides a clear path from contractors and internal specialists to the Project Manager, then to the Project Sponsor and Steering Committee, and ultimately to the CEO when required. It also allows specialist teams to communicate directly with relevant stakeholders while maintaining the Project Manager as the central coordination point.

6 Stakeholders

Successful delivery of the Network Infrastructure and Data Migration sub-projects depends on effective engagement with stakeholders who can influence the project or may be affected by its outcomes. Stakeholders will therefore be engaged according to their level of interest, influence and involvement. High-priority stakeholders will be involved closely in decisions and reviews, while other stakeholders will be kept informed or consulted where project activities may affect them.

Stakeholder engagement will remain flexible throughout the project. The project team will monitor stakeholder expectations, concerns and levels of involvement and adjust engagement approaches where required. The table below provides a synopsis of the external stakeholders who will be engaged (consulted with or informed) in the successful delivery of the project.

Key External Project Stakeholders			
Stakeholder Name/Group	**Interest in the Project**	**Engagement Required**	**Engagement Strategies**
DCPlus – Network Infrastructure Contractor	Responsible for the design, installation, configuration, testing and commissioning of the upgraded network infrastructure.	Manage Closely	Regular technical meetings, design reviews, progress updates, milestone reviews and early discussion of technical issues and dependencies.
DemSet – Data Migration Contractor	Responsible for data mapping, cleansing, test migration, production migration, validation and reconciliation.	Manage Closely	Migration workshops, data-quality reviews, progress meetings, test-result reviews and production migration readiness meetings.
Hardware and Software Vendors/Suppliers	Provide network hardware, software licences and technical support required for implementation.	Keep Satisfied / Keep Informed	Clear technical specifications, procurement communication, delivery updates and direct contact where supply or technical support issues arise.
Patients, Carers and Maternity Service Users	May be affected by service interruptions, migration activities and the reliability	Keep Informed / Consult where appropriate	Advance notification of planned disruptions, service updates, relevant training or support

	and security of the MSS environment.		information, and opportunities to provide feedback where required.
Regulatory and Compliance Stakeholders	Have an interest in the protection of health information and compliance with relevant privacy, security and regulatory requirements.	Keep Satisfied	Maintain appropriate compliance documentation and involve relevant privacy, security or legal representatives when required.

7 Communication Approaches

Communication will be managed so that stakeholders receive appropriate information at the right time and at a suitable level of detail. Communication will be clear, concise, consistent and appropriate to the needs of the intended audience. The project will use a combination of interactive, push and pull communication methods to support coordination, decision-making, reporting and access to project information.

Interactive communication will be used where discussion, clarification or decision-making is required. Push communication will be used for routine updates, formal notifications and progress information. Pull communication will be used where stakeholders require access to more detailed project documentation, reports and technical information.

7.1 Internal communication

Internal communication will support coordination between the Project Manager, Project Sponsor, CIO, technical leads, security personnel, quality and testing personnel and other members of the MSS project team. Project meetings and technical workshops will be used for collaboration, problem-solving and decision-making. Email, status reports and formal notifications will be used for routine updates and the communication of important project information. Shared project repositories will be used to provide access to approved plans, registers, reports and technical documentation.

Significant risks, issues, delays and proposed changes will be communicated to the Project Manager as soon as they are identified. Where necessary, these matters will be escalated through the appropriate governance structure. Important decisions, actions and approvals will be documented to maintain a clear and consistent project record.

Communication	Audience	Method	Frequency/Purpose	Owner
Project status update	Project team and relevant leads	Meeting and progress report	Fortnightly team review of progress, risks, issues and upcoming activities; monthly progress report to the Project Sponsor	Project Manager
Technical coordination	Relevant technical teams	Meeting/workshop	As required during design, installation, testing and migration	Relevant Technical Lead

Risk and issue communication	Project Manager and relevant decision makers	Register, meeting and email	When a significant risk or issue is identified	Risk/Issue Owner
Change requests	Project Manager, Change Control Board and affected leads	Change Request and review meeting	When a change is proposed	Project Manager
Milestone and readiness review	Project leads and approvers	Formal review meeting	At key project milestones and before major implementation activities	Project Manager

Communication effectiveness will be monitored throughout the project. The project team will review whether information is reaching the correct stakeholders, whether the frequency is appropriate and whether the selected communication method is effective. The approach will be adjusted where communication gaps or stakeholder concerns are identified.

7.2 External communication

External communication will be tailored to the needs of the relevant stakeholder group. DCPlus and DemSet will require regular two-way communication, as their activities are closely linked to the delivery of the Network Infrastructure and Data Migration sub-projects. Technical meetings, workshops, progress reviews and direct discussions will be used to clarify requirements, monitor progress, resolve issues and confirm readiness for major activities.

Hardware and software vendors will generally receive formal technical specifications, procurement information, delivery requirements and support requests. Direct communication will be used where delays, product issues or technical problems need to be resolved.

Patients, carers and maternity service users will receive clear and timely information where project activities may affect normal service delivery. This may include planned network outages, migration windows or temporary service limitations. Where consultation is appropriate, opportunities for feedback will be provided.

Regulatory and compliance stakeholders will receive relevant information and documentation as required, particularly when project decisions affect privacy, security, or the handling of health information. More detailed communication requirements, methods, responsibilities and frequencies will be documented in the separate Communication Plan.

8 Change Management Plan

A formal change-control process will be used to ensure that changes to the approved project baseline are assessed and authorised before implementation. This is important because changes to the Network Infrastructure or Data Migration sub-projects may affect scope, schedule, cost, resources, quality, security, data integrity, dependencies or readiness for go-live.

All significant changes will be recorded and assessed before a decision is made. Approved changes will then be incorporated into the relevant project documents and monitored through to completion.

8.1 Change Control Process

Step	Change Control Procedure
1. Identify the proposed change	A proposed change may arise from project monitoring, technical issues, schedule variation, stakeholder feedback, security concerns, data-quality findings or changes to project requirements.
2. Submit a Change Request	An authorised stakeholder submits a formal Change Request describing the proposed change, the reason for the request and the expected outcome.
3. Record the request	The Project Manager records the request in the Change Register and assigns it a unique reference number and status.
4. Assess the impact	Relevant project specialists assess the effect of the proposed change on scope, schedule, cost, resources, quality, security, data integrity, risks and dependencies.
5. Project Manager review	The Project Manager reviews the request and confirms that sufficient information and impact analysis have been provided.
6. Change Control Board review	Significant changes are submitted to the Change Control Board for review. The Board may approve, reject, defer or request further analysis of the proposed change.
7. Communicate the decision	The Project Manager records the decision and informs the requester and all affected stakeholders.
8. Implement approved change	Approved changes are assigned to the appropriate owner and incorporated into relevant project schedules, budgets, technical plans and other project documentation.
9. Verify and close	The Project Manager confirms that the approved change has been implemented correctly. The Change Register is then updated, and the change is formally closed.

8.2 Change Request Authority

Change requests may be submitted by the Project Manager, Project Sponsor, authorised project leads, DCPlus, DemSet or other authorised stakeholders where the proposed change affects their area of responsibility. Submitting a Change Request does not mean that the change has been approved. No significant change to the agreed project baseline will be implemented until it has been reviewed through the change-control process.

The Change Control Board (CCB) will be responsible for reviewing and making decisions on significant changes. The CCB is chaired by the Project Sponsor (Mr. Ben Dover) and includes the Project Manager, the Product Manager and the leads of the affected workstreams; changes beyond its authority are escalated to the Steering Committee. The CCB will consider the overall impact of each proposal rather than assessing only the area in which the change originated.

Role of the Change Control Board

The Change Control Board will:

- Review significant Change Requests and their supporting impact assessments;
- Consider the effect on scope, schedule, cost, resources, quality, security, risks and project dependencies;
- Determine whether the proposed change remains consistent with the objectives of the MSS project;
- Approve, reject, defer or request further analysis of a proposed change; and
- Ensure that approved changes are communicated and reflected in the relevant project documentation.

The Project Manager will coordinate the change-control process and act as the main point of communication between the requester, the CCB and affected stakeholders.

8.3 Change Tracking and Communication

Changes suggested will be all stored in a Change Register, such that they will all be traced and managed throughout the course of the project. It will include the following among others:

- ID of Change Request
- Date of request
- Requestor
- Change description and reason
- Workstream affected
- Impact evaluation
- Decision
- Approver
- Owner
- Status
- Date of closure

Once a change has been approved, affected stakeholders will be informed and the relevant project documents will be updated. Depending on the nature of the change, this may include the project schedule, budget, technical design, risk information, procurement documentation, migration plans or other project records. Any schedule-related change will also be reviewed for its effect on milestones, activity dependencies and project completion dates. This supports the schedule-control approach of monitoring progress, identifying variance and taking appropriate corrective action where required.

9 Quality Management Plan

The purpose of the Quality Management Plan is to describe how quality will be managed throughout the project's lifecycle. It also includes the processes and procedures for ensuring that quality planning, assurance and control are all conducted effectively.

Quality for Sub-Projects II and III will be managed through three linked activities. Quality planning sets the standards and acceptance criteria for each WS3 and WS4 deliverable during Initiation, Scoping and Planning & Design (Section 9.1). Quality assurance checks that the right processes are being followed, through design reviews, stage-gate reviews and audits of DCPlus and DemSet work against the agreed standards. Quality control tests the finished deliverables against measurable criteria, for example network performance, failover and penetration tests, and data reconciliation. Ash Mclelland (QA and Test Lead) coordinates quality activities and reports results to the Project Manager at the fortnightly project team meeting. Quality records (test plans, test results, defect logs, review minutes and sign-offs) are kept in the shared project repository.

9.1 Quality Expectations and Standards

The project must meet the following quality expectations and standards.

Product Quality Expectations	Sub-Project II (WS3) must deliver a secure, reliable and scalable network across the three identical sites (Perth, Rockingham and Mandurah) that supports the MSS SaaS platform, telehealth video and imaging, with a capacity for future growth. Sub-Project III (WS4) must deliver complete, accurate and secure patient data in the MSS platform, ready to support clinical and business operations from the Go-Live key milestone. Standards and processes to be applied: • Privacy Act 1988 (Cth) and the Australian Privacy Principles (APPs) • HL7/FHIR standards for health data exchange • ISO/IEC 27001-aligned security controls and the ACSC Essential Eight • ITIL service transition practices for cutover and handover Vendor best-practice configuration, MSI documentation standards and the change-control process (Section 8)
Acceptance criteria	Prioritised acceptance criteria: • Security and privacy: o No open critical/high findings from security assessment and penetration testing o Role-based access and MFA enforcement o Data encrypted in transit and at rest • Data accuracy: o 100% of in-scope records migrated (record counts reconcile) with a data error rate below 1% and no loss of clinical history • Availability and reliability: o Network availability of at least 99.5% during clinic hours o Failover to redundant links within 60 seconds in testing • Performance: o Latency under 50 ms between sites and enough bandwidth for concurrent telehealth video without degradation o Production data load completed within the agreed blackout windows • Supportability: o Configurations, network diagrams and IP plans documented o MSI IT staff trained to support the environment
Project-level quality tolerances	• SecurityL o Zero tolerance for open critical/high vulnerabilities at Go-Live o Medium findings accepted only with an approved fix plan within 30 days • Data accuracy: o Error rate of up to 1% (target 0%), but 0% for clinically critical fields such as medications and pregnancy history • Availability: o Up to 0.5% unplanned downtime per month during post-implementation monitoring (Sep–Nov 2027)

	• Performance: o Up to 10% variance from latency and throughput targets at peak times, provided telehealth sessions are not interrupted • Documentation: o Minor gaps allowed at Go-Live if corrected before WS3 close-out on 30 November 2027 Quality fixes that would delay a key milestone by more than two weeks, or exceed the contingency reserve, must go to the Change Control Board
Acceptance method	Acceptance is phased in line with the milestones in Section 4.2: • Scoping and high-level design deliverables are accepted at the business-case stage gate (30 Oct 2026) • Logical and physical designs, data quality assessment, cleansing and the migration strategy are accepted at the execute stage gate (30 Apr 2027), together with the SME-verified test-environment migration • Network deliverables are accepted once test and validation reports show the criteria are met (31 Aug 2027) • Migrated data is accepted through reconciliation, business process validation and CIO sign-off (14 Sep 2027) • Go-Live approval (30 Sep 2027) confirms all WS3 and WS4 products are approved • WS3 is finally accepted at close-out after post-implementation monitoring (30 Nov 2027) Each acceptance is recorded on a signed acceptance form stored in the project repository.
Acceptance responsibilities	• Ash Mclelland (QA and Test Lead): o Confirms test results meet the acceptance criteria • Don Morrison (Security & Compliance Expert): o Signs off security testing and compliance with confirmation of the security implementation by Don Lemon (Security Implementation Consultant) • Perera Kinley (Data Migration Expert): o Confirms reconciliation and data quality results • Catherine Dobbs (DCPlus) and Pardeep Kaur (DemSet): o Confirm contractor deliverables are complete • Dr Sara Adams (Product Manager): o Endorses that deliverables meet MSS product needs • Afra Binte Azad (Project Manager): o Coordinates acceptance and keeps acceptance records • Mr Ben Dover (Project Sponsor & CIO): o Gives final sign-off, CIO data sign-off and Go-Live approval

9.2 Quality Assurance and Quality Control

This section explains how the project will make sure that WS3 and WS4 deliverables meet the standards and stakeholder expectations set out above. Quality assurance focuses on the processes used to produce the deliverables, while quality control checks the deliverables themselves through testing, measurement and inspection.

Quality Goals	• Deliver a secure, scalable and reliable network that supports the MSS platform at all three sites • Migrate patient data completely and accurately, with an error rate below 1% • Comply with the Privacy Act 1988, the APPs and HL7/FHIR standards • Minimise disruption to maternity services during cutover and the production data load • Hand over a well-documented, supportable network environment to MSI's in-house IT team
Stakeholder Quality Expectations	• Patients and service users: ○ Health information is accurate, private and available when needed, with minimal service interruptions • Clinical users: ○ Fast, reliable access to complete patient records and stable telehealth connections • Project Sponsor (CIO): ○ Deliverables meet the acceptance criteria within budget and before Go-Live on 30 September 2027 • Contractors (DCPlus, DemSet): ○ Clear, stable requirements and timely reviews and sign-offs • QA team: ○ Testable requirements, access to test environments and time to fix defects before milestones • Project Manager: ○ Clear visibility of quality status, early warning of defects and documented sign-offs • MSI IT support team: ○ Complete documentation and training to support the network after close-out • Regulatory and compliance stakeholders: ○ Evidence that privacy and security obligations have been met
Quality Assurance Practices	• Agree a test strategy and quality checklist with DCPlus and DemSet before the business-case stage gate • Peer and expert reviews of the network logical/physical designs and data mapping specifications • Stage-gate quality reviews on 30 October 2026 and 30 April 2027, and a Go-Live readiness review • Regular process audits of contractor work against the contract, standards and this PMP • Independent security assessment and penetration testing, overseen by Don Morrison and Don Lemon • SME verification of the test-environment migration and a dry run of the production cutover • Change control and configuration management for all baselined documents • Lessons-learnt reviews at the end of each phase
Success Metrics	• Network availability ≥ 99.5% (clinic hours) and failover ≤ 60 seconds • Average latency between sites < 50 ms, no dropped telehealth video sessions in testing • 100% record-count reconciliation, data error rate < 1%, zero errors in critical clinical fields • Zero open critical/high security vulnerabilities at Go-Live

	• ≥ 95% of planned test cases executed and passed before each milestone, with no open Severity 1/2 defects • All high-priority defects closed within 5 working days • 100% of deliverables signed off by the nominated approver • ≥ 90% of targeted IT staff and end users trained before WS3 close-out
Quality Control Tools & Techniques	• Test management and defect tracking tool with traceability to requirements • Network monitoring and load-testing tools for performance and failover testing • Vulnerability scanning and penetration testing tools • Data profiling and reconciliation scripts comparing source and target record counts and checksums • Checklists, inspections and random sampling of migrated records • Pareto charts, cause-and-effect/fishbone diagrams and control charts to analyse defects and trends • Quality dashboard included in the monthly progress report to the Project Sponsor
Quality Principles/Values to Follow	• Quality is planned in from the start, not inspected in at the end • Focus on patients and clinicians as the end users of the system • Prevention over correction: find defects early through reviews • Decisions based on evidence and measured results • Continuous improvement through lessons learnt • Shared accountability: contractors and the internal team own the quality of their deliverables

10 Sustainability Management Plan

The purpose of this section is to help ensure that the MSS project team, contractors, and third-party providers manage this project in a sustainable way. It identifies potential sustainability issues and impacts, outlines our approach, assigned roles and responsibilities, our intended responses, and our reporting practices. This section will help support our commitment to economic growth, environmental protection, and social accountability.

The table below uses the P5 lens (People, Product, Process, Planet and Prosperity) to identify potential sustainability issues for Sub-Projects II and III, together with their potential impacts, proposed responses, expected outcomes, owners and the resources required to implement them.

P5 Element	Potential Sustainability Issue	Potential Impact	Proposed Response	Expected Outcome	Assigned Owner /Co-owner	Required Resources	Priority
People	Patient data privacy & equity of access	Breach of confidentiality, loss of trust and underserved groups excluded from digital care	Apply privacy-by-design to the network design and data migration, ensuring compliance with the Australian Privacy Principles (APPs). Provide low-bandwidth options and inclusive, accessible interfaces (WCAG 2.2) for regional, Aboriginal and CALD users. Check content for cultural appropriateness.	Improved trust, uptake, and equitable access	Owner: Don Morrison (Security & Compliance Expert) Co-owner: Bill Sykes (Legal Support)	Privacy impact assessment and legal review. Accessibility testing tool for WCAG compliance. Patient advocate and user input.	Very High
People	Staff workload and change fatigue during cutover, the production data load and Go-Live	Burnout, resistance to MSS, low adoption and more errors during transition	Schedule IT staff and end-user training in rostered blocks. Plan cutovers out of hours with fatigue limits.	Confident, supported staff. Smoother adoption; Fewer Go-Live errors	Owner: Afra Binte Azad (PM) Co-owner: Dr Sara Adams	Training time, super-users, backfill staff	High

			Provide floor support around Go-Live.				
Product	Network not scalable or not suited to low-bandwidth regional users. Hardware that becomes obsolete quickly	Early rework or replacement Poor telehealth quality and unequal access for regional, Aboriginal and CALD patients	Design for 3–5 years of growth, and choosing upgradable, vendor-supported equipment. Test telehealth under low-bandwidth conditions.	Longer asset life and consistent service quality across all three sites	Owner: Catherine Dobbs (DCPlus) Co-owner: Ash Mclelland	Capacity planning and load-testing tools, vendor lifecycle data	High
Process	Inefficient migration and cutover processes (repeated test loads, manual rework, extra copies of patient data)	Wasted effort and cost, data errors, schedule slippage and added privacy risk	Use automated, reusable migration scripts. Limit test data copies and securely delete them when finished. Apply change control and lessons learnt after each phase.	Fewer rework cycles, lower risk and a repeatable process for future markets	Owner: Perera Kinley Co-owner: Pardeep Kaur (DemSet)	Migration (ETL) tool, secure test environment, QA time	High
Planet	E-waste from replaced network hardware and higher energy use from new equipment	Landfill and hazardous waste, higher carbon emissions and power costs	Use certified e-waste recyclers. Securely wipe and reuse or donate working equipment. Specify energy-efficient devices. Prefer hosting providers using renewable energy.	Less e-waste and energy use, lower running costs	Owner: Catherine Dobbs (DCPlus) Co-owner: Afra Binte Azad	Recycling contractor, green procurement criteria, data sanitisation tools	Medium
Prosperity	Cost overruns or contractor delays reducing the financial return of the pilot Heavy reliance on external providers	Lower NPV and ROI, less funding for expansion, weak in-house capability	Track costs monthly using EVM against the Section 11 baseline. Hold the 10% contingency reserve.	Project stays within its $514,250 budget. Expected benefits (NPV ≈ $1.14M) protected.	Owner: Afra Binte Azad (PM) Co-owner: Bill Sykes (Legal Support)	Finance support, EVM reporting, contract management	High

			Include performance clauses in contracts. Use local WA suppliers where possible. Transfer knowledge to MSI IT.	Local jobs and in-house skills supported.			

11 Project Budget

The purpose of this section is to set out the estimated cost of delivering Sub-Project II (WS3 Network & Infrastructure) and Sub-Project III (WS4 Data Migration), broken down by activity and by quarter. The budget becomes the cost baseline against which actual spending is monitored and controlled, for example through Earned Value Management (EVM). The activities and their timing follow the work elements and schedule in Section 4 (Figure 1).

The budget for the overall implementation of subproject II and subproject III, as approved by the board, is as follows.

Basis of the estimates. The budget is derived from the ROM cost estimates in the MSS project scenario. Total ROM costs are $2,075,000 over Years 0–3 ($705,000, $590,000, $420,000 and $360,000), before discounting. The scenario allocates 10% of this budget to data migration and cleansing, which gives Sub-Project III a base budget of $207,500. It also allocates 25% ($518,750) to implementation services, which are shared between SaaS configuration and integration (Sub-Project I) and network and infrastructure work (Sub-Project II). Around half of this, $260,000, is allocated to Sub-Project II, including the network hardware for the three identical sites. In line with the scenario's 10% contingency allowance, each sub-project also carries a 10% contingency reserve, which is released only through the change-control process (Section 8).

Assumptions. All amounts are in Australian dollars and exclude GST. The budget covers six quarters in line with the project timeline: Q1 = Aug–Oct 2026, Q2 = Nov 2026–Jan 2027, Q3 = Feb–Apr 2027, Q4 = May–Jul 2027, Q5 = Aug–Oct 2027 and Q6 = Nov 2027–Jan 2028. Costs are allocated to the quarter in which each activity is scheduled to take place. Hardware and licences are purchased from Q3 (procurement of materials) so that equipment is available straight after the execute stage gate. As these are ROM-based estimates, variances of 25–40% may occur, and they will be refined as contractor quotes are received.

Sub-Project II: Quarterly Budget for the MSS Infrastructure Upgrade and Implementation

Expenditure (activity)	**Total Budget** ***(without GST)***	**Q1 Budget**	**Q2 Budget**	**Q3 Budget**	**Q4 Budget**	**Q5 Budget**	**Q6 Budget**
Current state assessment & infrastructure inventory	**$10,000**	$10,000	–	–	–	–	–
Business & technical requirements analysis	**$8,000**	$8,000	–	–	–	–	–
Gap analysis	**$4,000**	$4,000	–	–	–	–	–
Bill of materials	**$3,000**	$3,000	–	–	–	–	–
High-level network	**$9,000**	$9,000	–	–	–	–	–

architecture design							
Logical design (IP/VLAN plan, load balancing, security zones)	**$18,000**	–	$16,000	$2,000	–	–	–
Physical design (site survey, topology, racks, cabling)	**$16,000**	–	–	$16,000	–	–	–
Procurement of materials (routers, switches, firewalls, access points, cabling & network licences – 3 sites)	**$120,000**	–	–	$70,000	$50,000	–	–
Installation & commissioning (3 sites)	**$36,000**	–	–	–	$30,000	$6,000	–
Testing & validation (performance, failover, penetration testing)	**$12,000**	–	–	–	$12,000	–	–
Rollback & contingency plan	**$3,000**	–	–	–	$3,000	–	–
Post-implementation monitoring & documentation	**$12,000**	–	–	–	–	$9,000	$3,000
IT staff/end-user training & lessons learnt	**$9,000**	–	–	–	–	$5,000	$4,000
Contingency reserve (10%)	**$26,000**	$3,400	$1,600	$8,800	$9,500	$2,000	$700
Total Expenditure	**$286,000**	**$37,400**	**$17,600**	**$96,800**	**$104,500**	**$22,000**	**$7,700**

Sub-Project III: Budget for the MSS Data Migrations

Expenditure (activity)	**Total Budget** ***(without GST)***	**Q1 Budget**	**Q2 Budget**	**Q3 Budget**	**Q4 Budget**	**Q5 Budget**	**Q6 Budget**

Migration scope & existing data assessment	**$12,000**	$12,000	–	–	–	–	–
High-level data mapping, assumptions & DQ risk log	**$10,000**	$10,000	–	–	–	–	–
Detailed data mapping specifications	**$18,000**	$18,000	–	–	–	–	–
Data quality assessment & data cleansing (rules & cleansed data set)	**$45,000**	–	$45,000	–	–	–	–
Migration strategy, environments & schedule	**$12,000**	–	$6,000	$6,000	–	–	–
Data migration – test environment (migration tools/scripts, ETL licence)	**$40,000**	–	–	$40,000	–	–	–
Production cutover plan & environment preparation	**$20,000**	–	–	–	$20,000	–	–
Production data load & performance monitoring	**$26,000**	–	–	–	$26,000	–	–
Reconciliation & business process validation	**$18,500**	–	–	–	–	$18,500	–
Final report & lessons learnt	**$6,000**	–	–	–	–	$6,000	–
Contingency reserve (10%)	**$20,750**	$4,000	$5,100	$4,600	$4,600	$2,450	–
Total Expenditure	**$228,250**	**$44,000**	**$56,100**	**$50,600**	**$50,600**	**$26,950**	–

The combined budget for Sub-Projects II and III is $514,250 (excluding GST): $286,000 for the network infrastructure upgrade and $228,250 for data migration, including contingency. Spending is highest in Q3 and Q4 (Feb–Jul 2027), when network hardware is procured and installed and the test and production data migrations take place. Spending then falls in Q5 and Q6 as the work moves into reconciliation, post-implementation monitoring and close-out. The Project Manager Afra Binte Azad will

compare actual costs against this baseline each month, report variances to the Project Sponsor Mr. Ben Dover, and take any change in cost through the change-control process.
